Exhibit E-28

## Nevada Operations Office Critical Closure Path

(Timelines and Risk Data)

| Activity Description | Project | Risk | Milestone |
|---|---|---|---|
| **Nevada Test Site (NTS)** | | | |
| Resource Management Plan (RMP) Completed | Program Integration | (NA,5,1) | Resource Management Plan (RMP) Completed |
| State Agreement on Clean-up Levels - Soils | Soils | (3,3,3) | State Agreement on Clean-up Levels - Soils |
| Characterization, Treatment and Final Disposition of all NTS Mixed LLW | Mixed Low-level Waste | (2,1,3) | |
| Certification/Approval of the NTS TRU Waste Characterization Program and Shipment to WIPP | TRU/Mixed TRU | (4,2,5) | |
| Corrective Action Investigation Plan (Includes Value Of Information Analysis) | Underground Test Area | (2,2,1) | |
| Modeling Completed | Underground Test Area | (2,3,1) | Modeling Completed |
| Contaminant Boundary Defined | Underground Test Area | (2,3,1) | Contaminant Boundary Defined |
| Monitoring Network Design Completed | Underground Test Area | (2,3,1) | Monitoring Network Design Completed |
| Corrective Action Decision Document (Includes Well Program) | Underground Test Area | (2,3,1) | Corrective Action Plan Completed |
| Proof of Concept Completed | Underground Test Area | (3,2,1) | Proof of Concept Completed |
| Operation of WMD Low-level Program | Low-level Waste | (1,1,2) | |
| Program Management Support of LLW | Program Management | (1,1,2) | |
| Waste Management Programmatic Environmental Impact Statement Record of Decision (ROD) | Program Management | (NA,5,5) | Waste Management Programmatic Environmental Impact Statement LLW & MLLW RODs |
| **Nevada Off-sites Projects** | | | |
| Amchitka Surface Correction Action Decision Document | Off-sites | (2,3,2) | |
| Rulison Surface Closure Report | Off-sites | (1,1,2) | |
| Salmon Subsurface Closure Report | Off-sites | (1,1,2) | |
| Gnome Coach Subsurface Closure Report | Off-sites | (2,3,2) | |
| Shoal Subsurface Closure Report | Off-sites | (1,2,2) | |
| Gasbuggy Subsurface Closure Report | Off-sites | (2,3,2) | |
| Rio Blanco Surface Closure Report | Off-sites | (2,3,2) | |
| Central Nevada Test Area (CNTA) Subsurface Closure Report | Off-sites | (2,2,2) | |

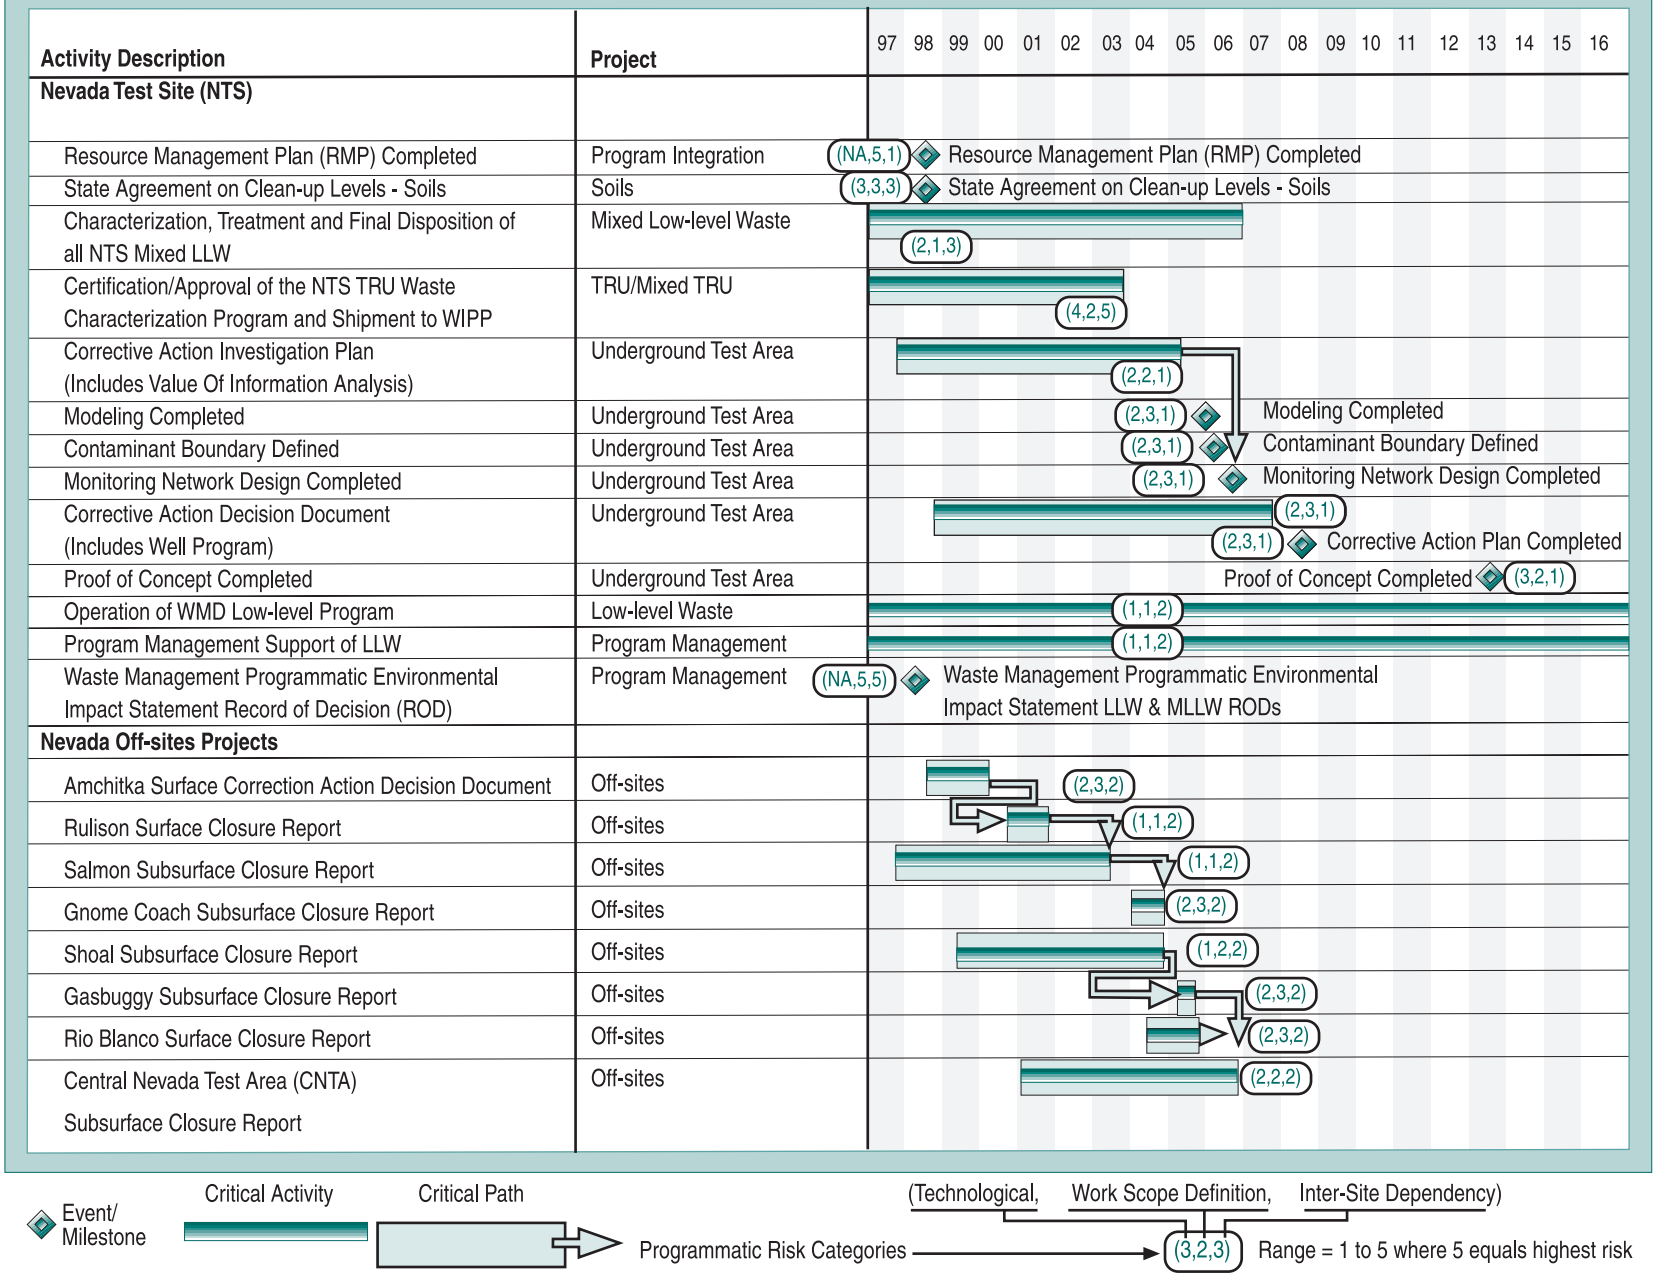

Event/ Milestone — Critical Activity — Critical Path

Programmatic Risk Categories (Technological, Work Scope Definition, Inter-Site Dependency) (3,2,3) Range = 1 to 5 where 5 equals highest risk
